MOTOROLA SOLUTIONS

Iowa Statewide Interoperable Communications System (ISICS)

Project Update

March 10, 2016

ISICS Project Flow

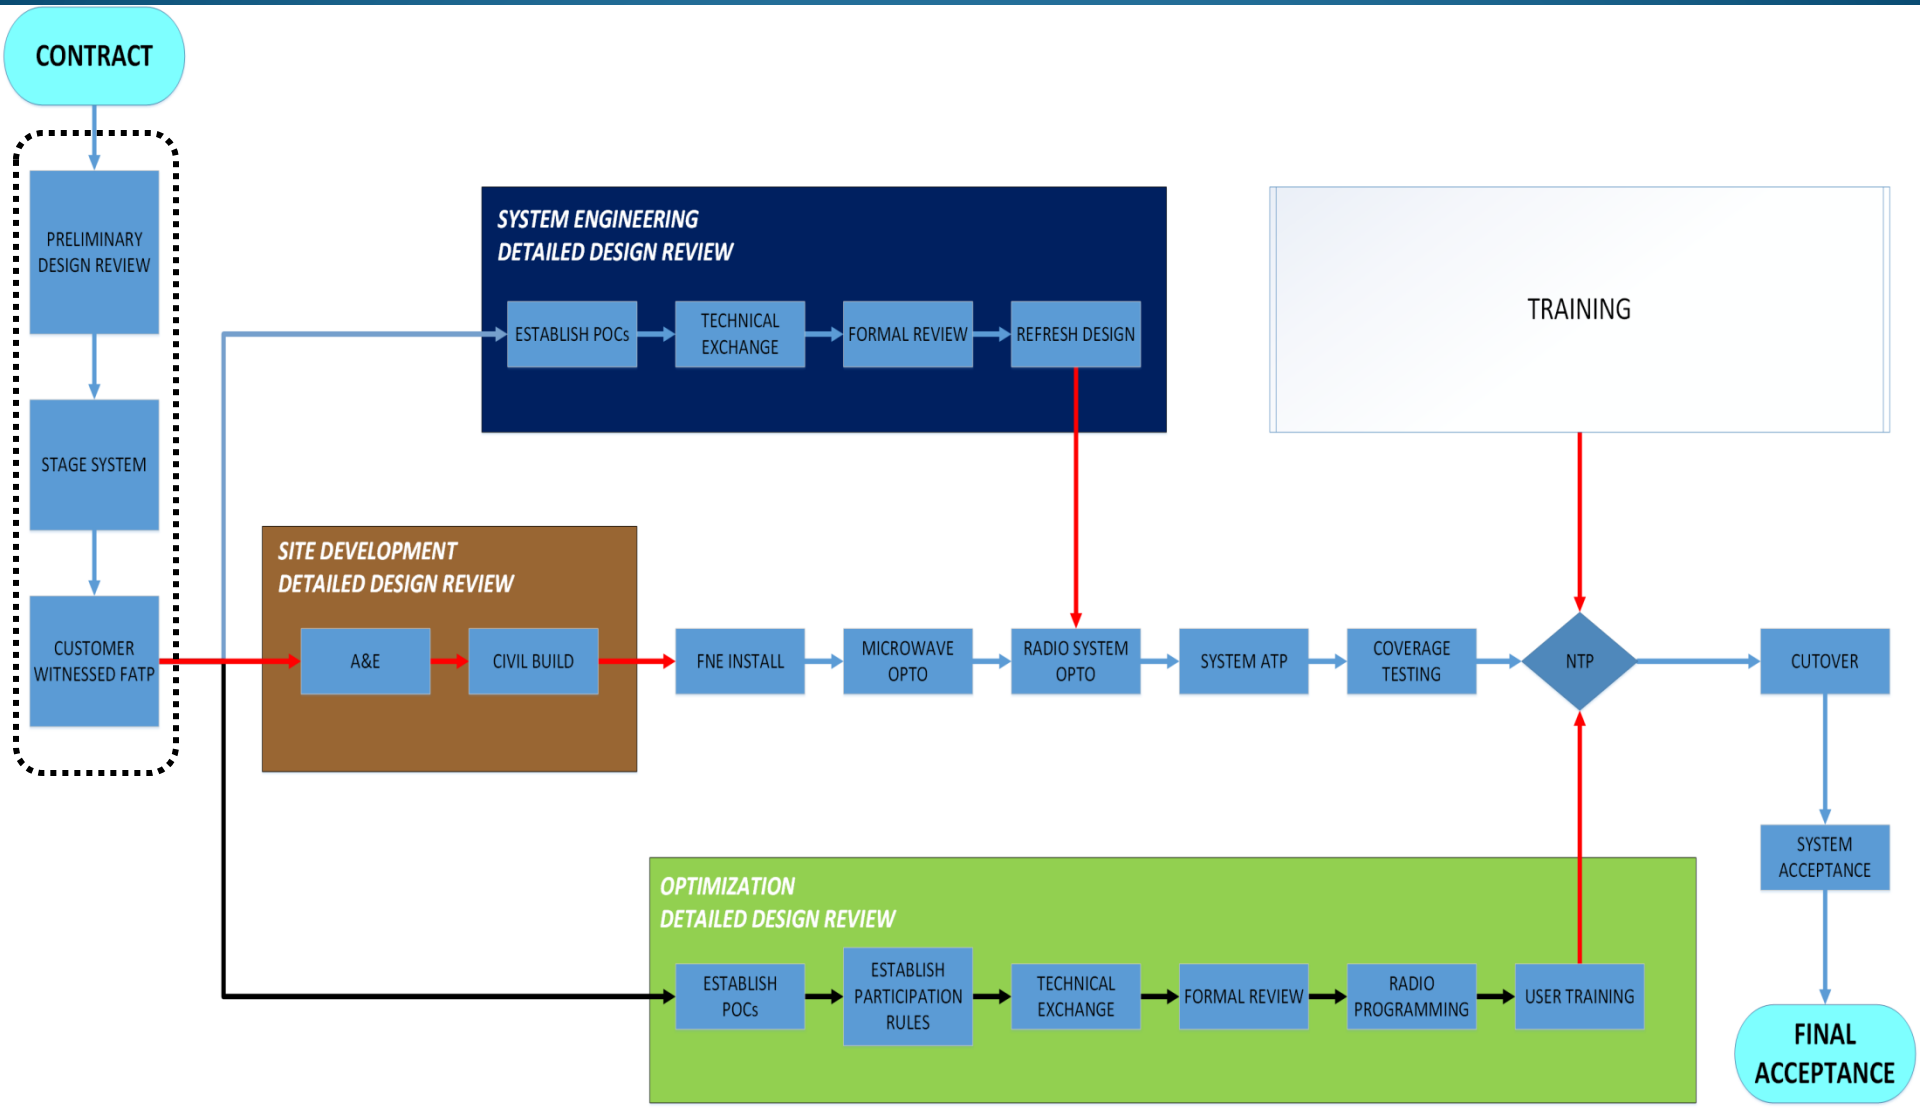

System Staging Event

Platform Shipped Warehouse

Platform Shipped Warehouse

ISICS Project Flow

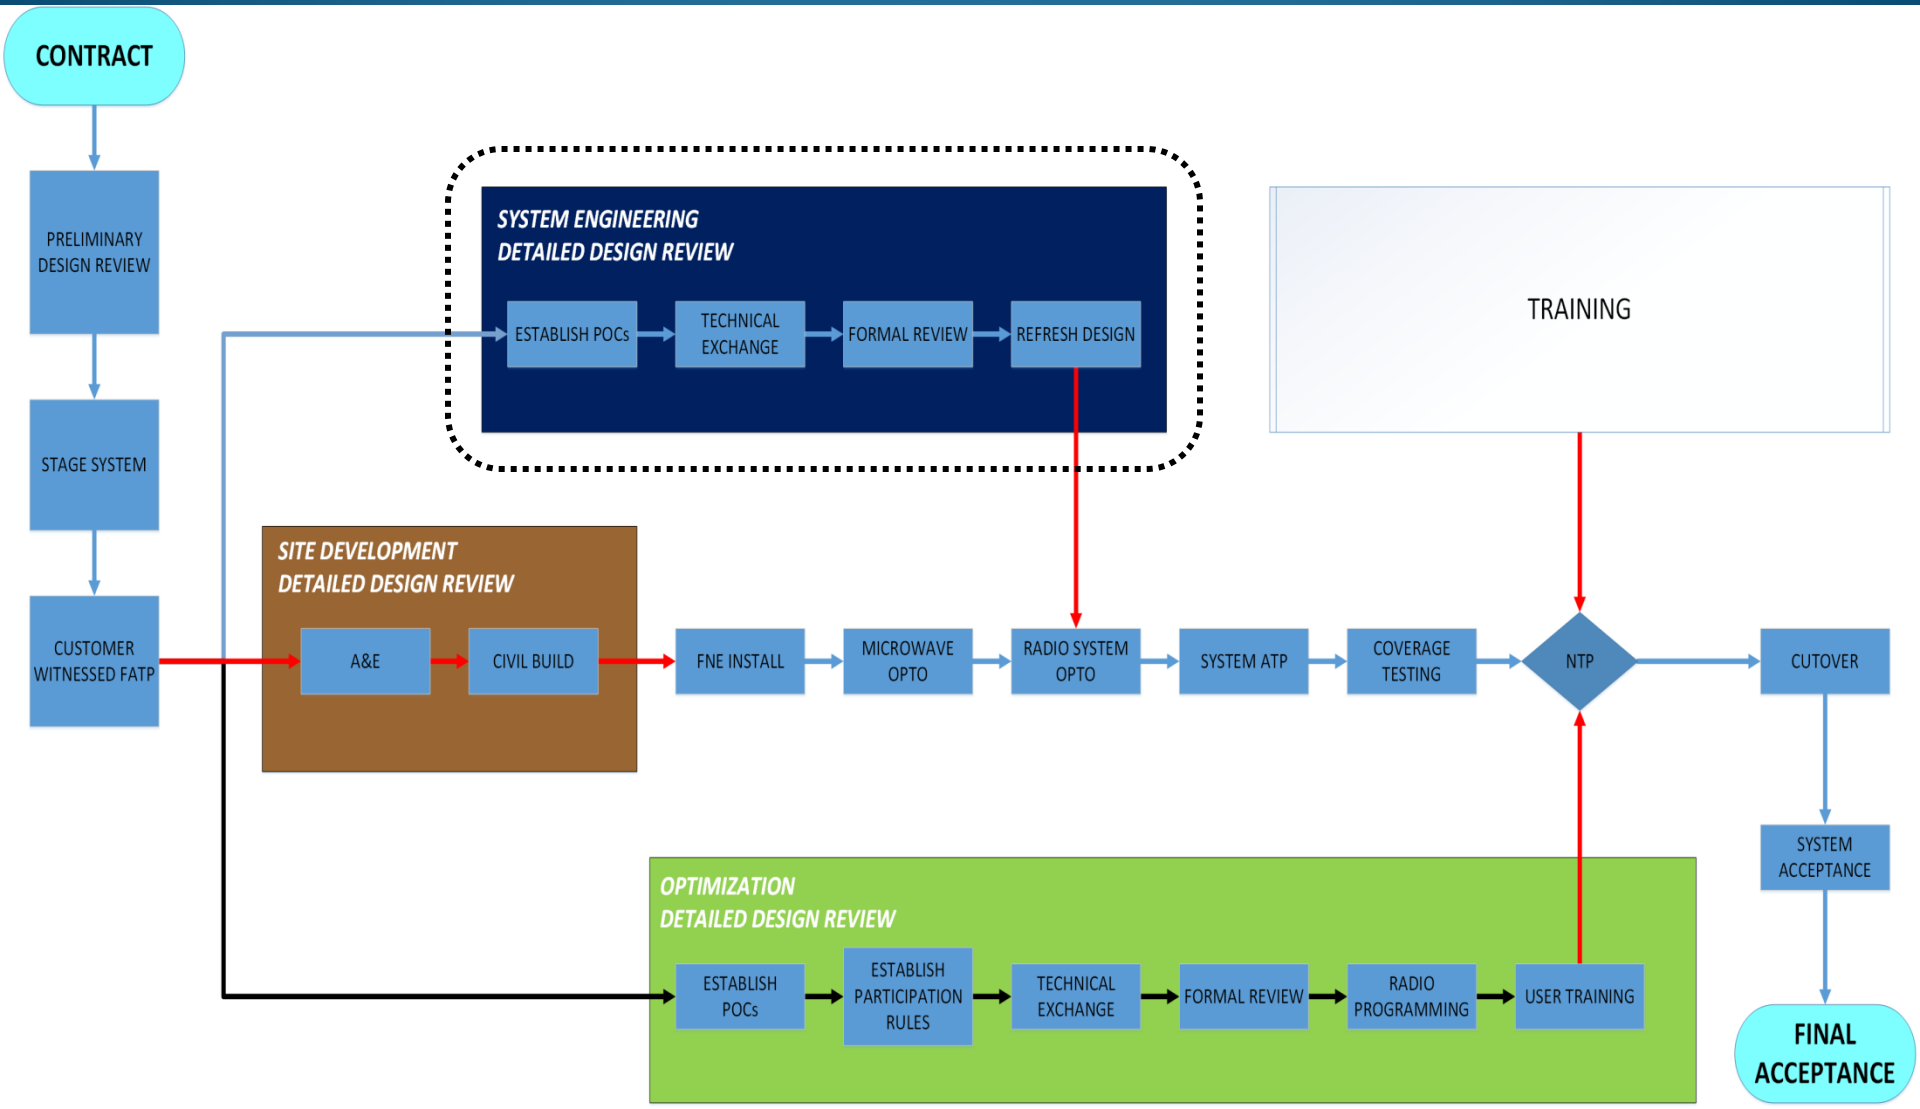

Engineering Design Review

- 2 DDRs held to date (more planned)
  - Operability/Interoperability
  - Management

Engineering Design Review

- 2 DDRs held to date (more planned)
  - Operability/Interoperability
  - Management
- DPS Aviation group
  - Operational needs
  - Physical equipment needs

Engineering Design Review

- 2 DDRs held to date (more planned)
  - Operability/Interoperability
  - Management
- DPS Aviation group
  - Operational needs
  - Physical equipment needs
- National Governors Association (NGA)
  - Operational needs
  - Physical equipment needs
- Other
  - Westcom, Woodbury, Dallas County, Des Moines, etc.

ISICS Project Flow

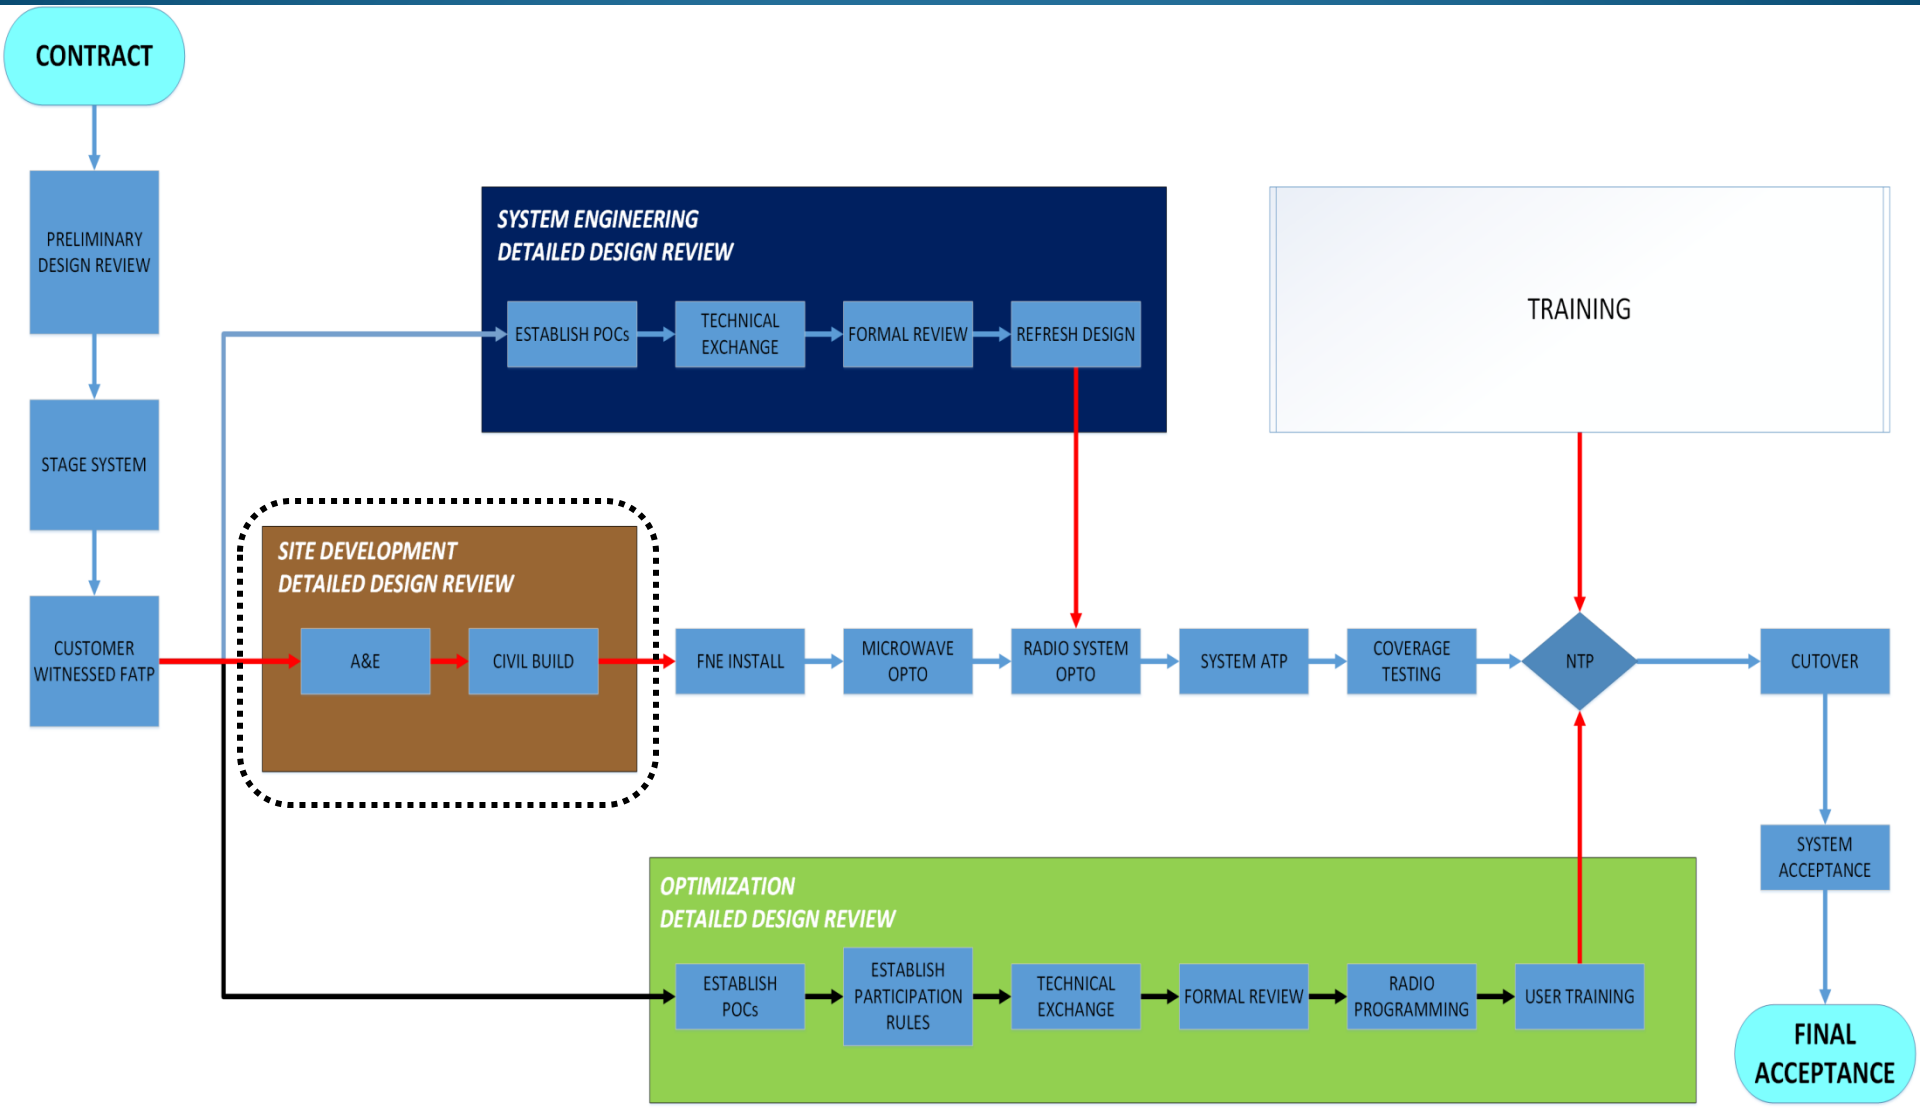

ISICS HL&EM Regions

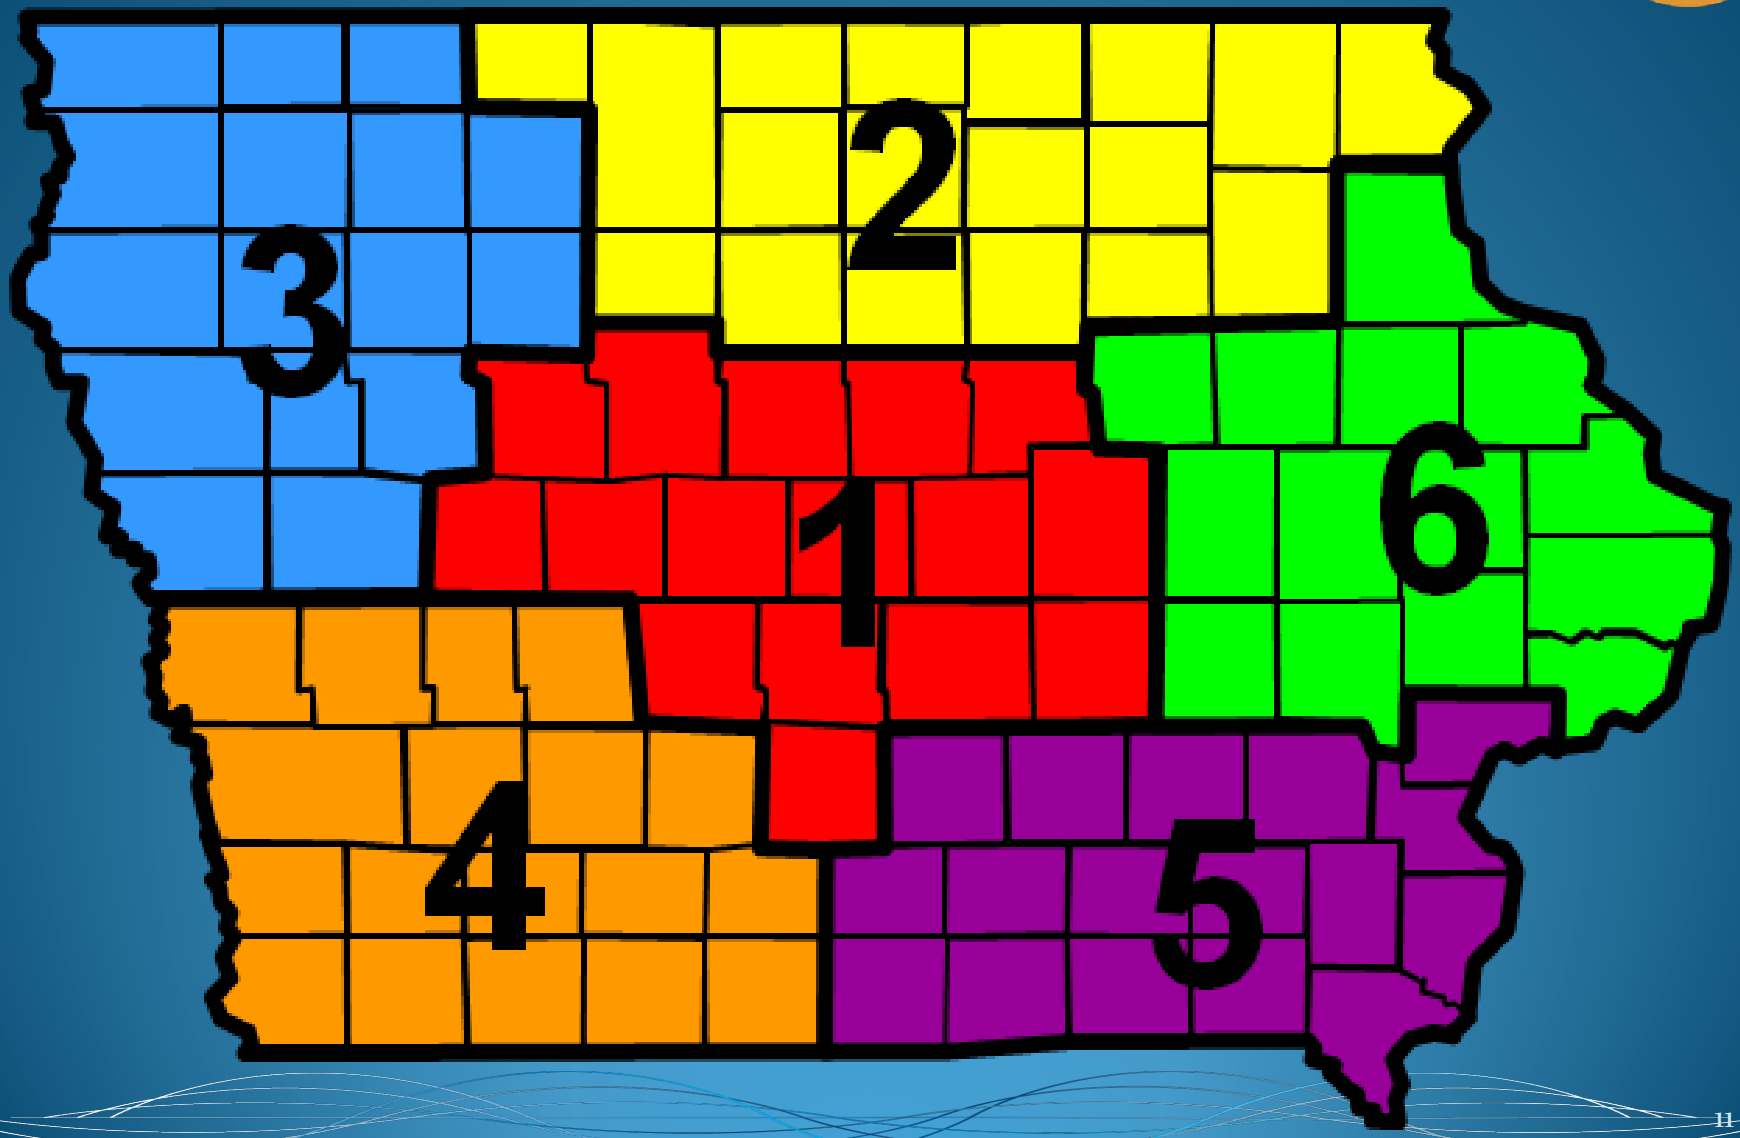

ARCHITECTURE & ENGINEERING DASHBOARD



Region 1 Site Pre-Construction	Site POC Identified	Formal A&E Visit	NEPA	SHPO	Mig Bird Public Notice	Structural Analysis	Modification Analysis	Power Plan	Final CDs	NTP
QTY	21	21	10	10	10	11	11	21	21	21
In-Process	1	0	2	0	0	4	0	0	8	0
Complete	20	18	0	0	0	0	0	0	0	0
% Complete	95%	86%	0%	0%	0%	0%	0%	0%	0%	0%

Region 2 Site Pre-Construction	Site POC Identified	Formal A&E Visit	NEPA	SHPO	Mig Bird Public Notice	Structural Analysis	Modification Analysis	Power Plan	Final CDs	NTP
QTY	12	12	6	6	6	6	6	12	12	12
In-Process	1	0	1	0	0	0	0	0	6	0
Complete	11	10	0	0	0	0	0	0	0	0
% Complete	92%	83%	0%	0%	0%	0%	0%	0%	0%	0%

Region 3 Site Pre-Construction	Site POC Identified	Formal A&E Visit	NEPA	SHPO	Mig Bird Public Notice	Structural Analysis	Modification Analysis	Power Plan	Final CDs	NTP
QTY	13	13	5	5	5	8	8	13	13	13
In-Process	2	0	1	0	0	1	0	0	6	0
Complete	11	8	0	0	0	0	0	0	0	0
% Complete	85%	62%	0%	0%	0%	0%	0%	0%	0%	0%

ARCHITECTURE & ENGINEERING DASHBOARD



Region 4 Site Pre-Construction	Site POC Identified	Formal A&E Visit	NEPA	SHPO	Mig Bird Public Notice	Structural Analysis	Modification Analysis	Power Plan	Final CDs	NTP
QTY	17	17	11	11	11	6	6	17	17	17
In-Process	2	0	0	0	0	1	0	0	6	0
Complete	15	15	0	0	0	0	0	0	0	0
% Complete	88%	88%	0%	0%	0%	0%	0%	0%	0%	0%

Region 5 Site Pre-Construction	Site POC Identified	Formal A&E Visit	NEPA	SHPO	Mig Bird Public Notice	Structural Analysis	Modification Analysis	Power Plan	Final CDs	NTP
QTY	12	12	9	9	9	3	3	12	12	12
In-Process	0	0	2	0	0	1	0	0	8	0
Complete	12	12	0	0	0	0	0	0	0	0
% Complete	100%	100%	0%	0%	0%	0%	0%	0%	0%	0%

Region 6 Site Pre-Construction	Site POC Identified	Formal A&E Visit	NEPA	SHPO	Mig Bird Public Notice	Structural Analysis	Modification Analysis	Power Plan	Final CDs	NTP
QTY	15	15	5	5	5	10	10	15	15	15
In-Process	0	0	0	0	0	4	0	0	6	0
Complete	15	15	0	0	0	0	0	0	0	0
% Complete	100%	100%	0%	0%	0%	0%	0%	0%	0%	0%

ACTION ITEMS

- Continue System Engineering DDR
- Complete agreements to support NGA
- Start installation process for NGA specific sites
- Preparations for 1st ISICS Core installation

Thanks!

IOWA STATEWIDE INTEROPERABLE COMMUNICATIONS SYSTEM

ISICS
